

COMPANY / UNIT

Sahney Kirkwood Pvt Ltd

DEPARTMENT

Production

ZONE

Zone 1 – Press

AUDIT DATE

08-09-2026

AUDITOR NAME

Rugved Marathe

ZONE LEADER

Sandeep Kothawade

MARKS

75 / 100

PERCENTAGE

75.0%

RATING


On Track

S-WISE SCORING

S	ACHIEVED	MAX	PERCENTAGE
1S – SEIRI (SORT)	15	20	75.0%
2S – SEITON (SET IN ORDER)	11	20	55.0%
3S – SEISO (SHINE)	17	20	85.0%
4S – SEIKETSU (STANDARDIZE)	16	20	80.0%
5S – SHITSUKE (SUSTAIN)	16	20	80.0%

5S PERFORMANCE WEB

AUDITOR VERIFICATION

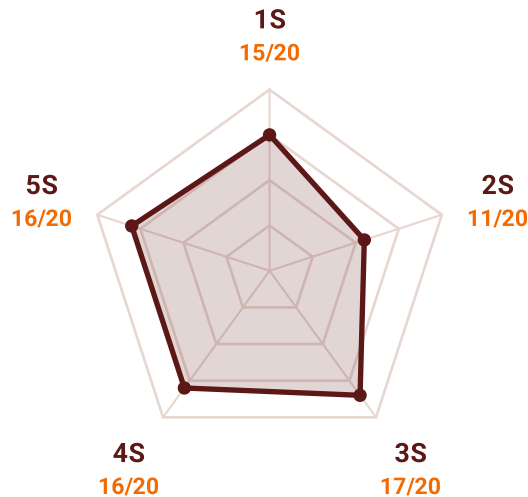

Each S shows achieved marks / applicable maximum; polygon uses percentage.

RATING SCALE

≥ 90% Outstanding

75–89% On Track

60–74% Improving

< 60% Needs Support

CHECKLIST – RESPONSES AND MARKS

Sr.	Check Point	Response	Marks
	1S – SEIRI (SORT)		15 / 20

1	Only materials required for the current production plan are at the line.	Progressing well	1
2	Unwanted tools, fixtures and change parts are removed from workstations.	Progressing well	1
3	Rejected parts are segregated in red bins and moved out at defined frequency.	Well implemented	2
4	Rework items are identified, quantified and stored in a marked area.	Well implemented	2
5	Obsolete formats, drawings and displays are removed from the line.	Well implemented	2
6	No excess consumables (gloves, cutting tools, spares) hoarded at stations.	Well implemented	2
7	Empty packaging, dunnage and trolleys are returned to designated areas promptly.	Progressing well	1
8	WIP between stations is within the defined standard quantity.	Well implemented	2
9	A red-tag area is defined near the line and cleared within the time limit.	Well implemented	2
10	No personal items at workstations.	Needs improvement	0
2S – SEITON (SET IN ORDER)			11 / 20
11	Line layout with marked locations for input, output and WIP material exists.	Needs improvement	0
12	Change-over parts / tooling are stored on labelled racks near the line.	Progressing well	1
13	Tools at stations are on shadow boards with outlines and labels.	Progressing well	1
14	Line-side bins are labelled with part number and standard quantity.	Progressing well	1
15	Material flow follows FIFO with visual indication (lanes, cards, boards).	Needs improvement	0
16	Fixtures, gauges and inspection instruments have designated protected locations.	Well implemented	2
17	Trolleys, pallets and handling equipment have marked parking locations.	Progressing well	1
18	Status identification (OK / Not OK / Under Inspection) tags are used correctly.	Progressing well	1
19	Production boards (plan vs actual, quality, OEE) are placed at defined locations.	Well implemented	2
20	Nothing is placed directly on the floor; all items on stands, pallets or bins.	Well implemented	2
3S – SEISO (SHINE)			17 / 20
21	Machines are cleaned as per the daily autonomous maintenance / CLIT schedule.	Progressing well	1
22	No oil, coolant, air or water leakage at machines and connections.	Progressing well	1
23	Machine guards, panels and covers are clean, intact and in place.	Well implemented	2
24	Floors around the line are free of chips, dust, oil and material spillage.	Well implemented	2
25	Sensors, limit switches and control panels are clean and dust-free.	Well implemented	2

26	Chip / scrap conveyors and bins are cleared before overflow.	Well implemented	2
27	Cleaning-cum-inspection reveals abnormalities which are tagged (fugui tags).	Well implemented	2
28	Lighting at workstations is adequate; fixtures are clean and working.	Well implemented	2
29	Coolant / lubricant condition is checked and maintained as per standard.	Progressing well	1
30	Cleaning materials are available at the line with a fixed storage place.	Well implemented	2
4S – SEIKETSU (STANDARDIZE)			16 / 20
31	One-point lessons / visual SOPs are displayed at workstations.	Well implemented	2
32	CLIT (Clean-Lubricate-Inspect-Tighten) standards are displayed at machines.	Well implemented	2
33	Quality standards / limit samples are displayed at inspection points.	Well implemented	2
34	Colour codes for bins, tags, pipelines and floor marking are standardized.	Well implemented	2
35	Standard WIP quantities and line-side stock norms are visually defined.	Progressing well	1
36	Abnormality tagging and escalation standard is defined and followed.	Needs improvement	0
37	Safety standards – LOTO, PPE matrix, machine safety signage – are displayed.	Well implemented	2
38	Daily 5S / start-up checklists are filled at every shift.	Well implemented	2
39	Skill matrix of operators is displayed and updated.	Well implemented	2
40	5S board with zone map, scores and improvements is maintained at the line.	Progressing well	1
5S – SHITSUKE (SUSTAIN)			16 / 20
41	Operators perform daily autonomous cleaning and inspection without fail.	Well implemented	2
42	Shift handover includes 5S condition of the line.	Well implemented	2
43	5S audits are done as per schedule; scores recorded.	Well implemented	2
44	Actions on previous audit findings are closed on time.	Well implemented	2
45	Operators follow SOPs and quality discipline consistently.	Progressing well	1
46	Abnormality tags raised are resolved within the target time.	Progressing well	1
47	Kaizens / suggestions from operators are generated and implemented.	Well implemented	2
48	Supervisors / managers conduct regular Gemba walks in the area.	Well implemented	2
49	5S is maintained during high production pressure (surprise check).	Well implemented	2
50	Line 5S score trend is stable or improving over the last 3 audits.	Needs improvement	0

	ZONE TOTAL (75.0%)		75 / 100
--	---------------------------	--	-----------------

NA is excluded from the applicable maximum. After-improvement evidence is managed separately and does not change these marks.
